

Gipsy Patch Lane

Progress Update and Outline Site Works Programme

SLG Presentation, April 2021

Gipsy Patch Lane works

April:

- Civils works for the upgrading of bus stops east of the railway bridge are nearing completion
- Trial pits for ground investigation & utilities locations
- Completed investigating of location of Bristol Water mains

Gipsy Patch Lane works

May/June:

- Complete bus stops east of the railway bridge
- Commence east of bridge drainage works (northern side)
- WPD diversion work – dates to be confirmed
- Bristol Water diversion work – dates to be confirmed

CPME Programme update

	2021				2022				2023
	Jan-Mar	Apr-Jun	Jul-Sept	Oct-Dec	Jan-Mar	Apr-Jun	Jul-Sept	Oct-Dec	Jan-Mar
Hatchet Road bus stops									
Install new shelters / Install iPoints and CCTV									
Gipsy Patch Lane bridge replacement & associated road works									
Road works at bridge, including road lowering and drainage									
Landscaping									
Gipsy Patch Lane East of Bridge									
metrobus stops:									
1. Bus Stop Construction East & Westbound stops									
Install metrobus shelters / Install iPoints and CCTV									
Road widening:									
Vegetation clearance									
2. Utility Diversions (South Side GPL - Smithcourt Drive / Bush Avenue)									
WPD tbc									
Bristol Water tbc									
Construction work									
3. North Side Highway Drainage									
4. North Side Surface Water Storage Pipes									
5a. South Side Widening (Eastern End)									
5b. South Side Widening (Central)									
5c. South Side Widening (Western End)									
6. Resurfacing & Completion									
Landscaping									
Gipsy Patch Lane West of Bridge									
Vegetation clearance									
Road widening construction work, including metrobus stops work									
1. North Side widening & drainage									
2. South Side works & drainage									
3. Resurfacing & Completion									
Install metrobus shelters / Install iPoints and CCTV									
Landscaping									
Construction Complete									

KEY:

- construction
- ▲ milestone reached
- ← change from last presentation

East of Bridge Construction Sequencing



Sequencing

- 1: Bus Stops
- 2: Utility Diversions
- 3: North side drainage
- 4: Stormwater storage pipes
- 5: South side widening
- 6: Resurfacing & completion

Utility Diversions

WPD
Bristol Water

Traffic Management Programme


Draft Emerging Traffic Management Programme for April 2021

Traffic management will remain under constant review	2021				2022				2023	KEY:
	Jan-Mar	Apr-Jun	Jul-Sept	Oct-Dec	Jan-Mar	Apr-Jun	Jul-Sept	Oct-Dec	Jan-Mar	
Hatchet Road bus stops										
Ad-hoc for shelter, iPoint and CCTV installation										
Gipsy Patch Lane bridge replacement & associated road works										
Full closure										
Partial opening (under review)										
Gipsy Patch Lane metrobus stops east:										
Partial closure and ad-hoc for iPoint and CCTV installation										
Road widening:										
Traffic management for Utility Diversions Smithcourt Drive / Bush Ave - tbc										
Traffic lights shuttle working Eastern side										
One-way system Pegasus Park to Little Stoke Lane										
Closure of side road jctns										
Ad-hoc for shelter, iPoint and CCTV installation										
Traffic Management removed										

KEY:
 traffic management
 ad-hoc traffic management

Gipsy Patch Lane Traffic Management

- ✓ Open
- ✓ Restricted
- ✗ Closed

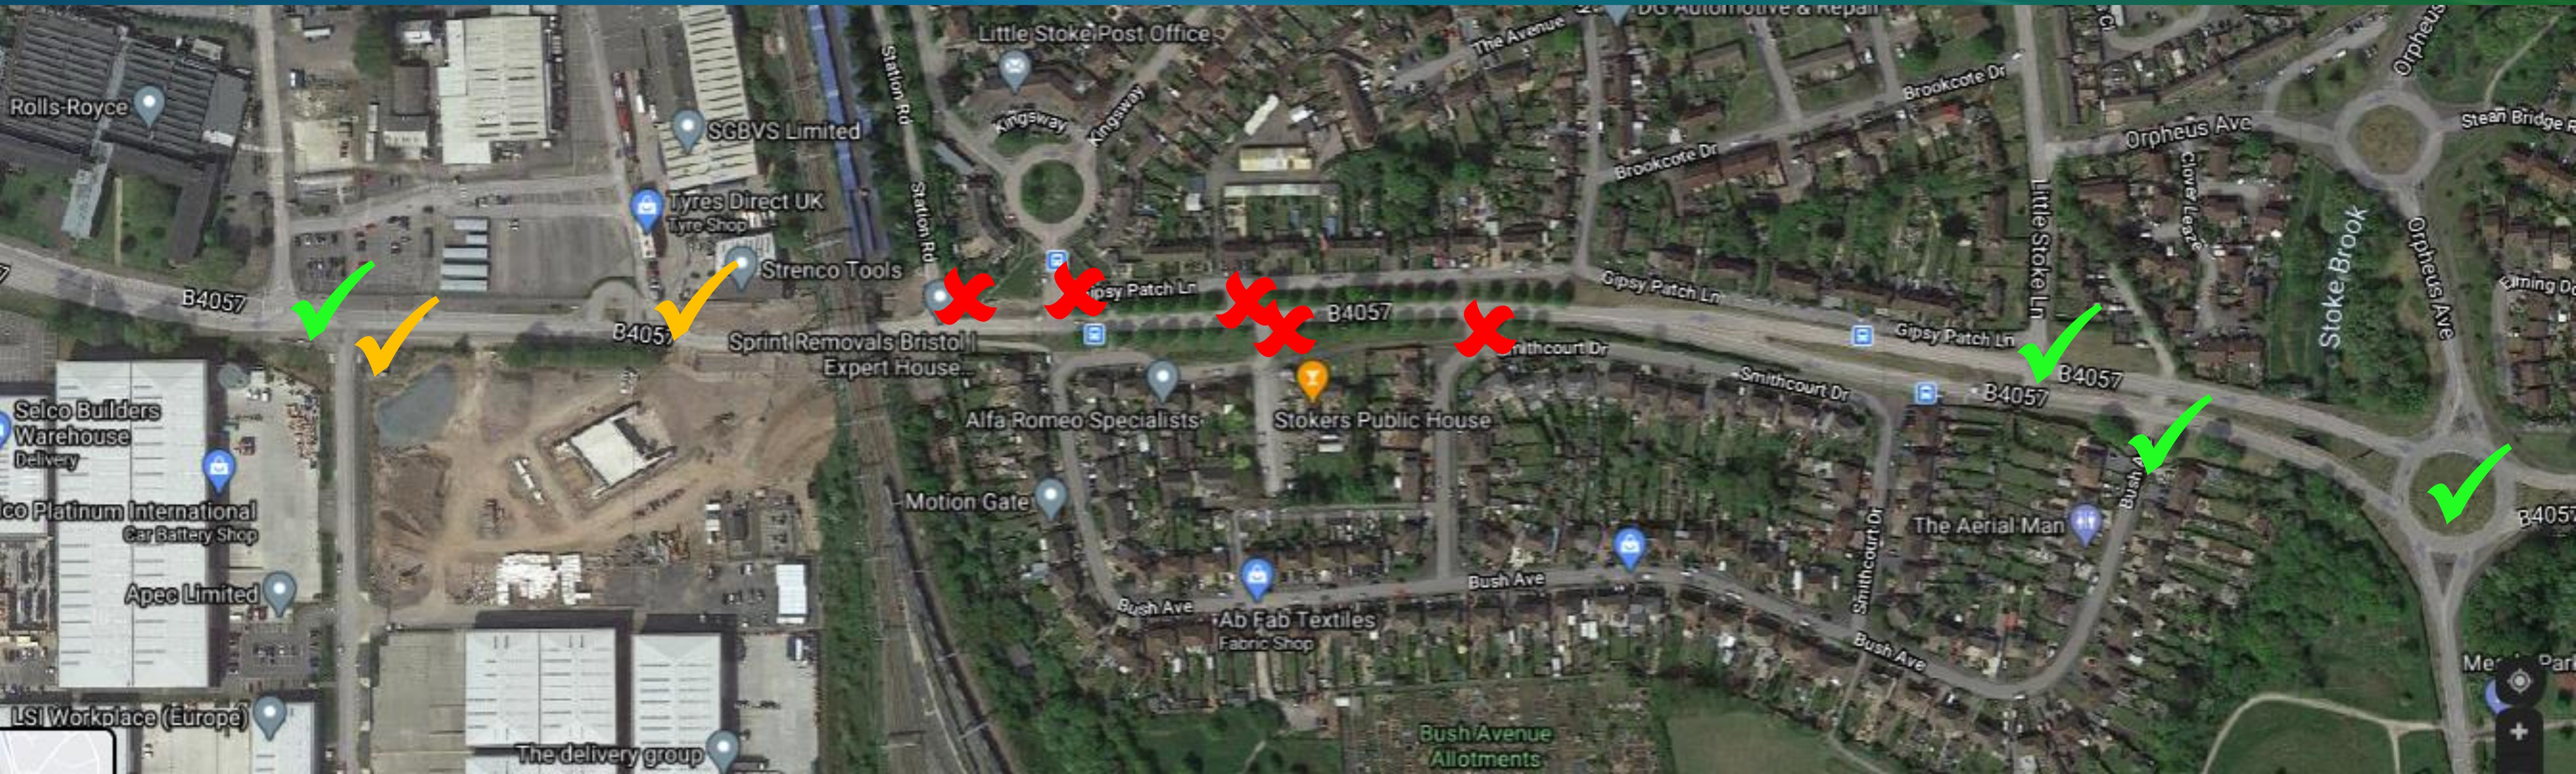

For more information, visit the project webpage

www.southglos.gov.uk/cpmetrobus

Or like and follow our Facebook page

www.facebook.com/sgloscpme
